ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		D01: Proposta de projecte	88 hrs	Mon 27/02/17	Sun 12/03/17	
2		D02: Estudi de viabilitat	6 days	Mon 13/03/17	Mon 20/03/17	
3		D03: Analsi I disseny de la solució	15 days	Tue 21/03/17	Mon 10/04/17	
4		P01: Creació del projecte	1 day	Tue 11/04/17	Tue 11/04/17	
5		P02: Creació del bundles	1 day	Tue 11/04/17	Tue 11/04/17	
6		P03: Creació de les entitats	2 days	Wed 12/04/17	Thu 13/04/17	
7		P04: Realació de les entitats	3 days	Thu 13/04/17	Mon 17/04/17	
8		P05: Creació de plantilla base	1 day	Mon 17/04/17	Mon 17/04/17	
9		P06: Creació de vistes del frontend	5 days	Mon 17/04/17	Fri 21/04/17	
10		P07: Creació de vistes del backend	5 days	Mon 24/04/17	Fri 28/04/17	
11		P08: Controladors I CRUDS	10 days	Mon 01/05/17	Fri 12/05/17	
12		P09: Login	1 day	Mon 15/05/1	Mon 15/05/1	
13		P10: Seguretat I restriccions	2 days	Tue 16/05/17	Wed 17/05/17	

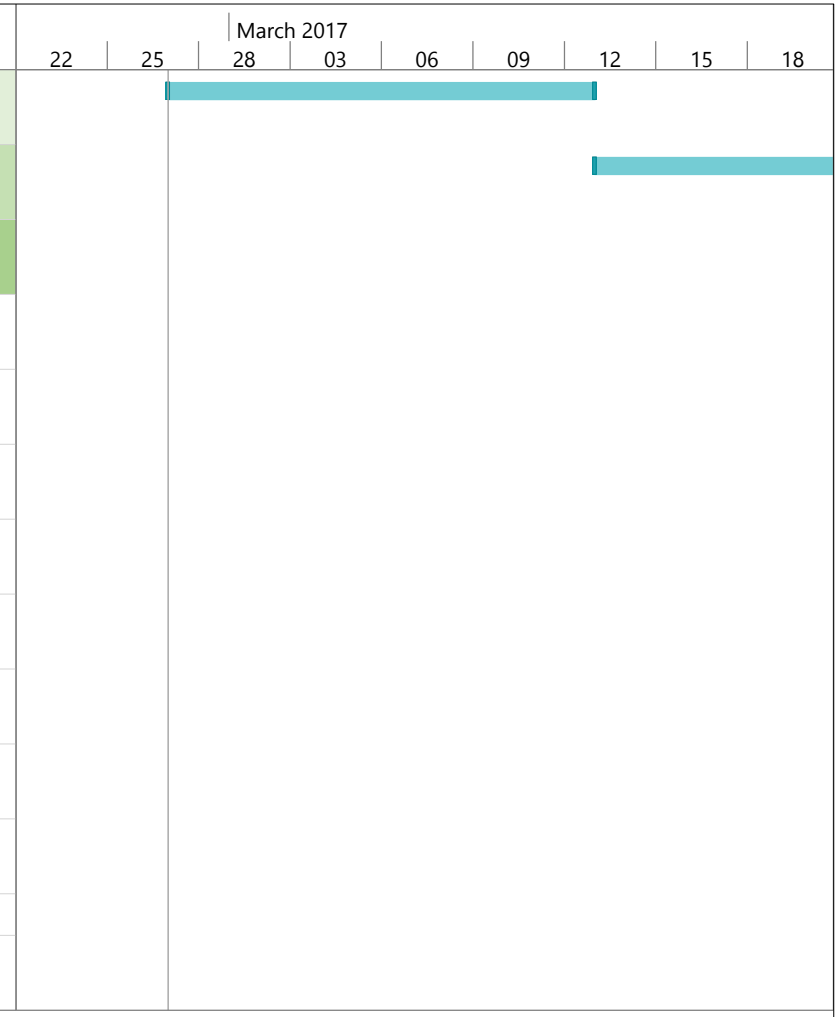

Project: Project1
Date: Mon 27/03/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
14		P11: Filtres	2 days	Wed 17/05/1	Thu 18/05/17	
15		P12: Pulir usabilitat del sistema	1 day	Fri 19/05/17	Fri 19/05/17	

March 2017

22 25 28 03 06 09 12 15 18

Project: Project1
Date: Mon 27/03/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

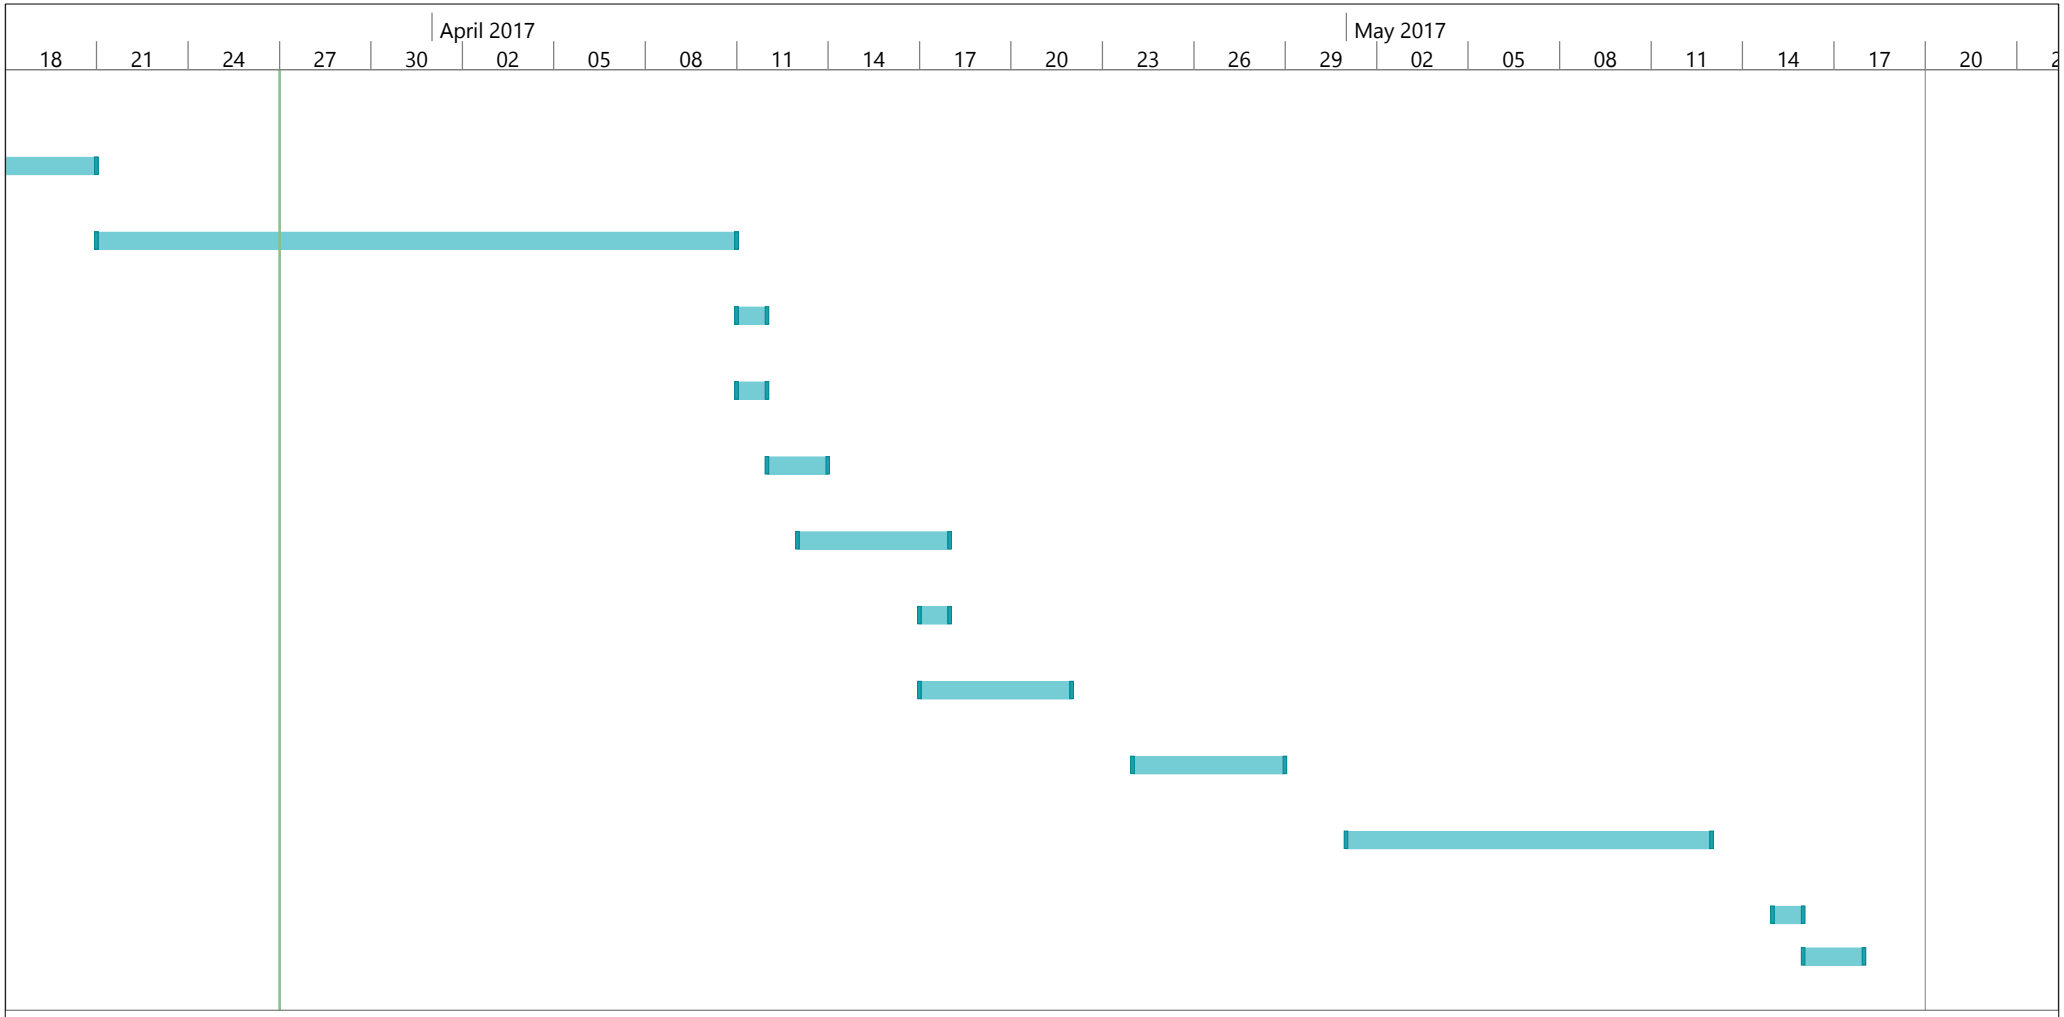

Project: Project1
Date: Mon 27/03/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	



Project: Project1
Date: Mon 27/03/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: Project1
Date: Mon 27/03/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

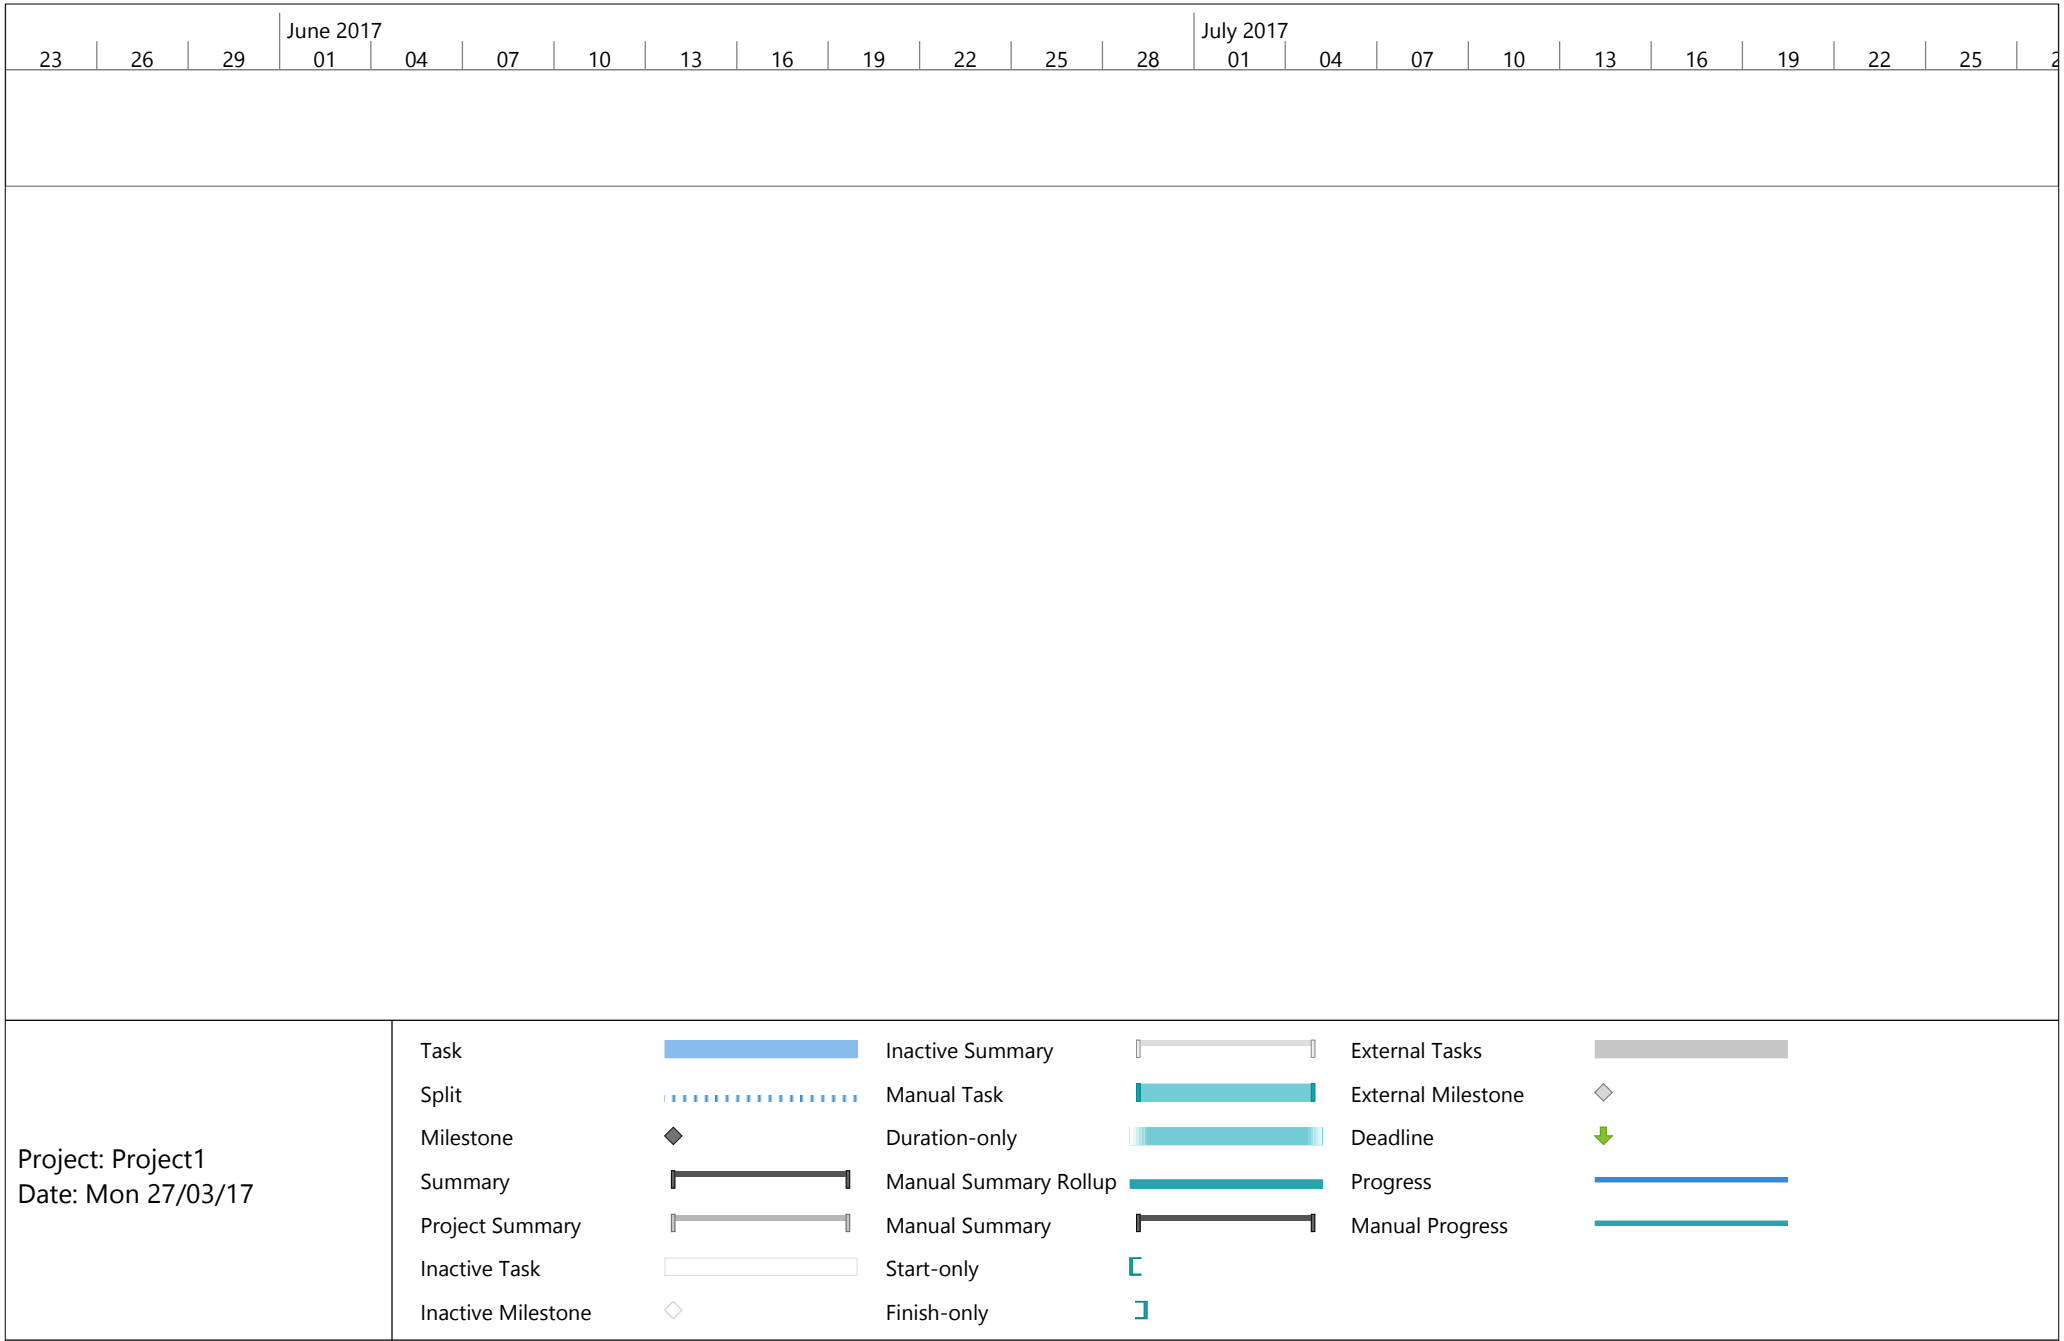
June 2017
July 2017
23
26
29
01
04
07
10
13
16
19
22
25
28
01
04
07
10
13
16
19
22
25
Project: Project1
Date: Mon 27/03/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
